



स्टील अथॉरिटी ऑफ इण्डिया लिमिटेड
STEEL AUTHORITY OF INDIA LIMITED
बोकारो इस्पात संयंत्र
BOKARO STEEL PLANT
एम.ओ.एम., चिड़िया
MOM, CHIRIA

Ref. No. MOM/PC/6/291

Date: 30.05.2025

To,
The Dy. Director General of Forest (C)
Regional Office
Ministry of Environment, Forest and Climate Change
2nd Floor, Headquarter – Jharkhand State Housing Board,
Harmu Chowk,
Ranchi – 834 002.

Sub: Six Monthly status of Compliance to the Conditions Stipulated in Environmental Clearance granted by MOEFCC for 4.20 MTPA Iron ore production from Mclellan Iron Ore Mining project of M/s SAIL vide letter No: J-11015/249/2009-IA. II(M), Dated: 23rd March 2011 for the period of October-2024 to March-2025.

Sir,

Please find the enclosed herewith the Six monthly compliance report for the period October-2024 to March-2025 with respect to the conditions stipulated by MOEFCC, GoI, New Delhi in the Environmental Clearance grant order of Manoharpur Ore Mines for production of 4.20 MTPA Iron ore production from Mclellan Iron Ore Mining project of M/s SAIL vide MoEFCC letter No: J-11015/249/2009-IA. II(M), Dated: 23rd March 2011.

It may, please be noted that mine is not in operation since 08.12.2005 for want of Stage II Forestry Clearance.

Thanking you.

Yours faithfully,
For, Steel Authority of India Ltd.

Ravi Ranjan
(Ravi Ranjan)

General Manager (Mining)
Manoharpur Ore Mines, Chiria
Bokaro Steel Plant (BSL), SAIL

Copy to:

1. Director, IA, MoEF&CC, GOI, Indira Paryavaran Bhavan, Aliganj, JorBagh Road, New Delhi -110003.
2. Member Secretary, JSPCB, HEC, Dhurwa, Ranchi – 834004.
3. In-charge, Eastern Zone, CPCB, Southern Conclave, Block 502, 5th & 6th Floors, 1582 Rajdanga Main Road, Kolkata - 700107 (W. B.)

Chiria Office : MOM Chiria, Po.-Ps : Chiria, W. Singhbhum, Jharkhand-833106, E-MAIL : momchiria@gmail.com, momperschiria@gmail.com

Head Office : Addm. Building, Bokaro Steel Plant, Bokaro City, Jharkhand - 827001

Regd. Office : Ispat Bhawan, Lodhi Road, New Delhi-110003, Phone : +91-11-2436-7481 (14 Lines), Fax : 24367015

हर किसी की जिन्दगी से जुड़ा हुआ है सेल

There's a little bit of SAIL in everybody's life

**Status of Compliance to Conditions Stipulated in
Environmental Clearance granted**

by

MoEFCC

Vide Order No:J-11015/249/2009-IA.II(M),

Dated:23rd March, 2011

for production of 4.20 MTPA

from

Mclellan Iron Ore Mining Project

(Period: October-2024 to March-2025)



STEEL AUTHORITY OF INDIA LIMITED

BOKARO STEEL PLANT (BSL)

MANOHARPUR ORE MINES

P.O. – CHIRIA, PIN : 833106

DIST. : SINGHBHUM (WEST)

JHARKHAND STATE



Environment Clearance letter No:J-11015/249/2009-IA.II(M), Dated: 23rd March, 2011 of Mclellan Iron Ore Mining project for production of 4.20 MTPA (ROM) of Iron ore.

Half yearly compliance report for the period: October-2024 to March-2025

A. Specific Condition

Sl. No.	Condition	Compliance Status as on March' 2025
i	The project proponent shall obtain Consent to Establish and Consent to Operate from the Jharkhand State Pollution Control Board and effectively implement all the conditions stipulated therein.	Consent to Establishment was obtained from Jharkhand State Pollution Control Board for a capacity of 4.20 MPTA, vide letter Ref. no: PC/NOC/JSR/26/10/G-172, dated: 25.01.2016.
ii	Environmental clearance is subject to final order of the Hon'ble Supreme Court of India in the matter of Goa Foundation Vs. Union of India in Writ Petition (Civil) No. 460 of 2004, as may be applicable to this project.	Noted.
iii	Environmental clearance is subject to obtaining clearance under the Wildlife (Protection) Act, 1972 from the competent authority, as may be applicable to the project.	Not Applicable
iv	Environmental clearance is subject to obtaining clearance under Forest (Conservation) Act, 1980 for diversion of forestland. Mine working shall be restricted to the area for which forestry clearance has been obtained.	Stage-1 Forest Clearance was obtained vide letter Ref: F. No.8-70/2009-FC, dated: 09.03.2011. For mine working over 379.228 ha. Stage-01 conditions compliances submitted & Grant of Final Clearance is awaited.
v	Prior environmental Clearance from the Standing Committee of the National Board for wildlife shall be obtained due to location of the mine within the core zone of Singhbhum Elephant Reserve, before starting any activity relating to the project at site. All the conditions stipulated by the standing committee shall be effectively implemented in the project. It shall be noted that wildlife clearance shall be granted to the project and that your proposal for wildlife clearance shall be considered by the competent authority ties on its merits and decision taken. The investment made in the project, if any based on environmental clearance granted to the project, in anticipation of the clearance from wildlife clearance shall be entirely at the cost and risk of the project proponent and Ministry of Environment and Forests shall not be responsible in this regard in any manner.	Not Applicable.



Sl. No.	Condition	Compliance Status as on March' 2025
vi	The Mining operations shall be restricted to above the groundwater table and it should not intersect the groundwater table. In case of working below the groundwater table, prior approval of the Ministry of Environment and Forests and the Central Ground Water Authority shall be obtained, for which a detailed hydro-geological study shall be carried out.	<p>Water table level at our mining lease area is about 400 m AMSL and ultimate depth of our proposed workings will be above 438 m AMSL. Hence there is no possibility for intersecting of Mine workings with the ground water table.</p> <p>Due to any reason it is required to work below the groundwater table, we will obtain prior approval of the Ministry of Environment and Forests and the Central Ground Water Authority shall be obtained, for which a detailed hydro-geological study will be carried out.</p>
vii	The project proponent shall ensure that no natural watercourse and/or water resources shall be obstructed due to any mining operations. The first order streams and the seasonal nallahs originating from the mining lease area shall be protected.	<p>No working during October-2024 to March-2025.</p> <p>Proper Precautions will be taken to avoid obstructions to Natural water resources by providing drains and bounds etc. at required places during operations period.</p>
viii	The top soil, if any shall temporarily be stored at earmarked site(s) only and it should not be kept unutilized for long. The topsoil shall be used for land reclamation and plantation.	<p>No working during October-2024 to March-2025.</p> <p>After starting operations, the top soil will be temporarily stored at earmarked site. The stored top soil will be used in plantation works.</p>
ix	The over burden (OB) generated during the mining operations shall be stacked at earmarked dump site(s) only and it should not be kept active for a long period of time and their phase-wise stabilization shall be carried out. There shall be two external over burden dumps having maximum projected height of 7 m and 32 m. The maximum height of the dumps shall not exceed 32 m having two terraces and the overall slope of the dump shall be maintained to 28. The OB dump should be scientifically vegetated with suitable native species to prevent erosion and surface run off. In critical areas, use of geo textiles shall be undertaken for stabilization of the dump. Monitoring and management of rehabilitated areas shall continue until the vegetation becomes self-sustaining. Compliance status shall be submitted to the Ministry of	<p>No working during October-2024 to March-2025.</p> <p>After starting operations the over burden (OB) generated during the mining operations will be stored at earmarked site. Phase-wise stabilization will be carried out.</p> <p>Six monthly Compliance Status is being submitted to the Ministry of Environment & Forests and Climate Change and its Regional Office located at Ranchi.</p>



Sl. No.	Condition	Compliance Status as on March' 2025
	Environment & Forests and its Regional Office located at Bhubaneswar on six monthly basis.	
x	Catch drains and siltation ponds of appropriate size shall be constructed around the mine working soil, mineral and OB dump(s) to prevent run off of water and flow of sediments directly into the Hamsadagaar Nallah, the Koina River, the seasonal nallahs and other water bodies. The water so collected should be utilized for watering the mine area, roads, green belt development etc. The drains shall be regularly de-silted particularly after the monsoon and maintained properly. Garland drains, setting tanks and check dams of appropriate size, gradient and length shall be constructed around the mine pit, soil, mineral and over burden dumps to prevent run off of water and flow of sediments directly into the Hamsadagaar Nalla, the Koina River, the seasonal nallahs and other water bodies and sump capacity should be designed keeping 50% safety margin over and above peak sudden rainfall (based on 50 years data) and maximum discharge in the area adjoining the mine site. Sump capacity should also provide adequate retention period to allow proper settling of silt material. Sedimentation pits shall be constructed at the corners of the garland drains and de-silted at regular intervals.	<p>No working during October-2024 to March-2025.</p> <p>After starting operations, Repair of old Retaining wall, Garland drain, siltation pond and construction of new Retaining wall, Garland drain, siltation pond at required places will be carried out .</p>
xi	Dimension of the retaining wall at the toe of the over burden dumps and the OB benches within the mine to check run-off and siltation shall be based on the rain fall data.	<p>No working during October-2024 to March-2025.</p> <p>Dimension of the retaining wall and check dams will be designed based on the rainfall data.</p>
xii	Plantation shall be raised in an area of 367.228 ha including a 7.5 m wide green belt in the safety zone around the mining lease, over burden dumps, backfilled and reclaimed area, mine benches, along the roads etc. by planting the native species in consultation with the local DFO/Agriculture Department. The density of the trees should be around 2500 plants per ha. Greenbelt shall be developed all along the mine lease area in a phased manner and shall be completed within first five years.	<p>No working during October-2024 to March-2025.</p> <p>Greenbelt will be developed all along the mine lease area in a phased manner and shall be completed within first five years after the start of mining operations.</p>



Sl. No.	Condition	Compliance Status as on March' 2025																					
xiii	Effective safeguard measures, such as regular water sprinkling shall be carried out in critical areas prone to air pollution and having high levels of particulate matter such as around loading and unloading point and all transfer points. Extensive water sprinkling shall be carried out on haul roads. It should be ensured that the Ambient Air Quality parameters conform to the norms prescribed by the Central Pollution Control Board in this regard.	<p>No working during October-2024 to March-2025.</p> <p>Regular water sprinkling will be done on haul roads, loading and unloading point and all transfer points during operation period.</p>																					
xiv	The project authority should implement suitable conservation measures to augment ground water resources in the area in consultation with the Regional Director, Central Ground Water Board.	<p>As the mine pits are located at the hill top, all the surface runoff from the mining areas have been diverted to mine pits, from where it seeps in to the ground.</p> <p>Check bunds, Garland drains and siltation pond has been constructed to control surface runoff.</p>																					
xv	Regular monitoring of ground water level and quality shall be carried out in and around the mine lease by establishing a network of existing wells and installing new piezometers during the mining operation. The periodic monitoring [(at least four times on a year-pre-monsoon (April-May), monsoon (August), post-monsoon (November) and winter (January); once in each season)] shall be carried out in consultation with the State Ground Water Board/Central Ground Water Authority and the data thus collected may be sent regularly to the Ministry of Environment and Forest and its Regional Office Bhubaneswar, the Central Ground Water Authority and the Regional Director, Central Ground Water Board. If at any stage, it is observed that the groundwater table is getting depleted due to the mining activity; necessary corrective measures shall be carried out.	<p>Network of 6 nos. of existing Dug Wells located around the mines have been selected for ground water level monitoring. Ground water table levels at the selected wells are being monitored at regular intervals i.e. 4 times in a year.</p> <p>The Range of water levels during Post Monsoon and during winter is as follows,</p> <table border="1"> <thead> <tr> <th>ID</th><th>Location</th><th>Water level below the Ground Surface (in meters)</th></tr> </thead> <tbody> <tr> <td>G1</td><td>Adjacent to community centre at Anqua</td><td>6.15- 6.30</td></tr> <tr> <td>G2</td><td>Opposite to community centre at Anqua</td><td>6.30-6.40</td></tr> <tr> <td>G3</td><td>Near Anqua Model Steel Village Gate</td><td>1.90-2.10</td></tr> <tr> <td>G4</td><td>Siva Mandir</td><td>3.25-3.35</td></tr> <tr> <td>G5</td><td>Near CNI Church</td><td>7.95-8.00</td></tr> <tr> <td>G6</td><td>Near Bisra Chowk</td><td>1.70-1.80</td></tr> </tbody> </table> <p>In addition to above Two piezometers one at Chiria (150 feet) and another at Dhobil</p>	ID	Location	Water level below the Ground Surface (in meters)	G1	Adjacent to community centre at Anqua	6.15- 6.30	G2	Opposite to community centre at Anqua	6.30-6.40	G3	Near Anqua Model Steel Village Gate	1.90-2.10	G4	Siva Mandir	3.25-3.35	G5	Near CNI Church	7.95-8.00	G6	Near Bisra Chowk	1.70-1.80
ID	Location	Water level below the Ground Surface (in meters)																					
G1	Adjacent to community centre at Anqua	6.15- 6.30																					
G2	Opposite to community centre at Anqua	6.30-6.40																					
G3	Near Anqua Model Steel Village Gate	1.90-2.10																					
G4	Siva Mandir	3.25-3.35																					
G5	Near CNI Church	7.95-8.00																					
G6	Near Bisra Chowk	1.70-1.80																					



Sl. No.	Condition	Compliance Status as on March' 2025
		<p>Village 200 feet provided and are being monitored at regular intervals i.e. 4 times in a year.</p> <p>Monitoring data of Groundwater level and Surface water quality is being submitted to Central ground Water Authority and Central Ground Water Board, Ranchi. Ground water levels during Post Monsoon and during Winter and piezometer photograph is placed in Annexure – 1.</p>
xvi	Regular monitoring of the flow rate of the springs and perennial nallahs flowing in and around the mine lease shall be carried out and records maintained.	<p>No working during October-2024 to March-2025.</p> <p>Regular monitoring of flow rate of water at the perennial nalla i.e. Hamsadagaar Nalla, is being done and records are being maintained.</p>
xvii	The Project proponent shall obtain necessary prior permission of the competent authorities for drawl of requisite quantity of water (surface water and ground water) required for the project.	Permission obtained from Water Resource Department, Govt. of Jharkhand and agreement has been made with Water Ways Division, Chaibasa for drawl of water from Hamsadagara Nalla to the tune of 0.62 MCM per annum for Manoharpur Ore Mines, Chiria, with validity up to 02.08.2027.
xviii	Suitable rainwater harvesting measures on long term basis shall be planned and implemented in consultation with the Regional Director, Central Ground Water Board.	<p>As the mine pits are located at the hill top, all the surface runoff from the mining areas have been diverted to mine pits, from where it seeps in to the ground.</p> <p>Check bunds, Garland drains and siltation pond has been constructed to control surface runoff.</p>
xix	Appropriate mitigative measures shall be taken to prevent pollution of the Koina River in consultation with the State Pollution Control Board.	<p>No working during October-2024 to March-2025.</p> <p>As the mine pits are located at the hill top, all the surface runoff from the mining areas have been diverted to mine pits, from where it seeps in to the ground.</p> <p>Comprehensive Catchment Area Treatment (CAT) Plan for Saranda Forest area fed by Karo & Koina river system (which includes Gua & Chiria mines of</p>



Sl. No.	Condition	Compliance Status as on March' 2025														
		SAIL) was approved by PCCF (HoFF), GoI on 01.02.2022 with total financial outlay of Rs. 12286.307 lakh (all mines located in Saranda) to be utilized for execution of different work items. Accordingly, DFO, Saranda vide letter dated 28.11.2022 directed to deposit an amount of Rs. 5.43 crores for all leases of Manoharpur Ore Mines (including Dhobil lease) which was deposited by SAIL on 29.11.2022 towards implementation of recommendation related to Bio-conservation, Eco-restoration & Infrastructures as per approved CAT Plan.														
xx	Vehicular emissions shall be kept under control and regularly monitored. Measures shall be taken for maintenance of vehicles used in mining operations and in transportation of mineral from mine face to the beneficiation plant. The vehicles shall be covered with a tarpaulin and shall not be overloaded.	No working during October-2024 to March-2025. Will be followed during operation.														
xxi	No blasting shall be carried out after the Sunset; Blasting operation shall be carried out only during the daytime. Controlled blasting shall be practiced. The mitigative measures for control of ground vibrations and to arrest fly rocks and boulders should be implemented.	No working during October-2024 to March-2025. Will be followed during operation.														
xxii	Digital processing of the entire lease area using remote sensing technique should be done regularly once in three years for monitoring land use pattern and report submitted to the Ministry of Environment and Forests and its Regional Office located at Bhubaneswar.	<p>The entire mine lease is in Ankua RF of Saranda Forest Division.</p> <p>Land use and land cover map of Mclellan lease area have been developed by Department of Mining Engineering Indian Institute of Technology (Indian School of Mines) Dhanbad as on January 2025 and Land use pattern of the lease area is as follows,</p> <table><tr><th>LU/LC classes</th><th>Area (ha)</th></tr><tr><td>Mine lease Boundary</td><td>823.617</td></tr><tr><td>Dense forest</td><td>680.355</td></tr><tr><td>Open forest</td><td>27.890</td></tr><tr><td>Mining Area</td><td>31.100</td></tr><tr><td>Built-up area</td><td>1.862</td></tr><tr><td>Barren/Waste Land</td><td>82.410</td></tr></table>	LU/LC classes	Area (ha)	Mine lease Boundary	823.617	Dense forest	680.355	Open forest	27.890	Mining Area	31.100	Built-up area	1.862	Barren/Waste Land	82.410
LU/LC classes	Area (ha)															
Mine lease Boundary	823.617															
Dense forest	680.355															
Open forest	27.890															
Mining Area	31.100															
Built-up area	1.862															
Barren/Waste Land	82.410															



Sl. No.	Condition	Compliance Status as on March' 2025
xxiii	Drills shall either be operated with dust extractors or equipped with water injection system.	No working during October-2024 to March-2025. Will be followed during operation.
xxiv	Mineral handling area shall be provided with adequate number of high efficiency dust extraction system. Loading and unloading areas including all the transfer points should also have efficient dust control arrangements. These should be properly maintained and operated.	No working during October-2024 to March-2025. Will be followed during operation.
xxv	Sewage treatment plant shall be installed for the colony. ETP shall also be provided for the workshop and wastewater generated during the mining operation.	<p>Septic Tanks with soaking pits have been provided for the various accommodations. Septic Tank & Soaking Pits are being cleaned regularly and maintained.</p> <p>5KLD STP & 5KLD ETP has been installed and put in operation from 25.02.2025. at SAIL Chiria Hospital. Photographs showing the 5KLD STP & 5 KLD ETP are placed at Annexure-2.</p> <p>For Supply, Installation, Testing, Commissioning and maintenance of 30 KLD STP at Chiria township Open Tender Enquiry was issued vide Ref No: BSL/JGOM/CC/18 of 2024-25 dated 29.03.2025 and four parties submitted bids. Installation of 30KLD STP will be completed by 31st December-25.</p> <p>Since 1998, the mine is operated through Composite Mining contractor and all the HEMM and equipment were deployed by the contractor. Most of maintenance jobs are done at their work shop at Rourkela/Manoharpur.</p> <p>However, Vehicle washing facility with Oil grease traps was provided at Chiria general office for vehicles.</p>
xxvi	Pre-placement medical examination and periodical medical examination of the workers engaged in the project shall be carried out and records maintained. For the purpose, schedule of health examination of the workers should be drawn and followed accordingly.	Pre-placement medical examination and periodical medical examination is being carried out and records maintained.



Sl. No.	Condition	Compliance Status as on March' 2025
xxvii	<p>The project proponent shall take all precautionary measures during mining operation for conservation and protection of endangered fauna namely elephant, sloth bear, Indian wolf, python etc. spotted in the study area. Action plan for conservation of flora and fauna shall be prepared and implemented in consultation with the State Forest and wildlife Department. Necessary allocation of funds for implementation of the conservation plan shall be made and the funds so allocated shall be included in the project cost. All the safeguard measures brought out in the wildlife Conservation Plan so prepared specific to the project site shall be effectively implemented. A copy of action plan shall be submitted to the Ministry of Environment and Forests and its Regional Office, Bhubaneswar.</p>	<p>All the precautions are under taken for not to disturb the flora and fauna in the mining lease area. Necessary facilities are being extended to local forest department for their inspection and monitoring of forest area. IWLMP for West Singhbhum District of Jharkhand was prepared by an Expert Committee constituted by the State Govt. vide notification dated 27.08.2011. SAIL was assigned responsibility for institutionalizing and funding the study. After submission of report on IWLMP by the Committee, GoJ vide letter dated 19.09.2014 forwarded to MoEFCC, GoI. MoEFCC vide order dated 26.08.2014 constituted a Multi-Disciplinary Expert Committee (MDEC) to examine IWLMP. IWLMP was again refined and revised IWLMP was finally submitted by the Expert Committee to GoJ and MoEFCC, GoI on 10.03.2016. Final IWLMP was appraised in 45th meeting of Standing Committee of National Board for Wildlife on 04.09.2017 wherein the committee appreciated the IWLMP.</p> <p>MPSM was approved by MoEFCC on 08.06.2018 wherein it has been stated that the prescription of IWLMP prepared and approved by the State Wildlife Authority, National Board of Wildlife (NBWL) and Project Elephant (PE) of MoEFCC must be followed. IWLMP was presented before GoJ on 29.10.2018. Further the compliance of the observations pointed was submitted by SAIL to GoJ on 01.02.2019. Further, GoJ vide letter dated 30.04.2019 raised certain queries, which was replied on 31.05.2019.</p> <p>IWLMP is pending with GoJ for approval. Realization of money towards implementation of IWLMP shall be collected from lease holders.</p>



Sl. No.	Condition	Compliance Status as on March' 2025
		SAIL has submitted an undertaking to abide by the guidelines and contribute fund for implementation of IWLMP on prorate basis.
xxviii	The entire mining lease area shall be fenced by erecting solar powered electric fencing all round it. The fencing so erected shall be maintained properly and the cost towards erection and maintenance of the solar powered electric fencing shall be borne by the project proponent out of the project cost.	As the project area falls within the RF, the matter has been discussed with forest officials. State Forest Department officials are of the opinion that Solar fencing may obstruct/ effect the movement of wild life animals. Accordingly, the matter is being discussed with DFO, Saranda Division and a request letter has been submitted to DFO, Saranda on 24.03.2023, 28.06.2023 and 12.03.2024. Based on the opinion of the State Forest Department, action will be taken for compliance of the condition.
xxix	No transportation of ore outside the mine lease area shall be carried out after the sunset.	No working during October-2024 to March-2025. Will be followed during operation.
xxx	The critical parameters such as RSPM (Particulate matter with size less than 10 um i.e. PM10) and NOx in the ambient air within the impact zone, peak particle velocity at 300m distance or within the nearest habitation, whichever is loser shall be monitored periodically. Further, quality of discharged water shall also be monitored (TDS, DO, PH and Total Suspended Solids (TSS). The monitored data shall be uploaded on the website of the company as well as displayed on a display board at the project site at a suitable location near the main gate of the Company in public domain. The Circular No. J-20012/1/2006-IA (M) dated 27.05.2009 issued by Ministry of Environment and Forests, which is available on the website of the Ministry www.envfor.nic.in , shall also be referred in this regard for its compliance.	No working during October-2024 to March-2025. Will be followed during operation.
xxxi	A Final Mine Closure Plan along with details of Corpus Fund should be submitted to the Ministry of Environment & Forests 5 years in advance of final mine closure for approval.	Not Applicable at present. Final Mine closure plan along with the fund details will be submitted to the ministry 5 years advance.

**B. General Conditions**

Sl. No.	Condition	Compliance as on March' 2025
i	No change in mining technology and scope of working should be made without prior approval of the Ministry of Environment & Forests.	No working during October-2024 to March-2025.
ii	No change in the calendar plan including excavation, quantum of mineral iron ore and waste should be made.	No working during October-2024 to March-2025.
iii	Four ambient air quality-monitoring stations should be established in the core zone as well as in the buffer zone for RSPM (Particulate matter with size less than 10um i.e. PM10) and NOx monitoring. Location of the stations should be decided based on the meteorological data, topographical features and environmentally and ecologically sensitive targets and frequency of monitoring should be undertaken in consultation with the State Pollution Control Board.	No working during October-2024 to March-2025.
iv	Data on ambient air quality RSPM (Particulate matter with size less than 10um i.e., PM10) & NOx should be regularly submitted to the Ministry of Environment and Forests including its Regional office located at Bhubaneswar and the State Pollution Control Board/Central Pollution Control Board once in six months.	No working during October-2024 to March-2025.
v	Fugitive dust emissions from all the sources should be controlled regularly. Water spraying arrangement on haul roads, loading and unloading and at transfer points should be provided and properly maintained.	No working during October-2024 to March-2025.
vi	Measures should be taken for control of noise levels below 85 dBA in the work environment. Workers engaged in operations of HEMM, etc. should be provided with ear plugs/muffs.	No working during October-2024 to March-2025.
vii	Industrial waste water (Workshop and waste water from the mine) should be properly collected, treated so as to conform to the standards prescribed under GSR 422(E) dated 19 th May, 1993 and 31 st December, 1993 or as amended from time to time. Oil and grease trap should be installed before discharge of workshop effluents.	No working during October-2024 to March-2025.



Compliance status of ES

Information on Ongoing Project

Sl. No.	Condition	Compliance as on March' 2025																										
viii	Personnel working in dusty areas should wear protective respiratory devices and they should also be provided with adequate training and information on safety and health aspects. Occupational health surveillance program of the workers should be undertaken periodically to observe any contractions due to exposure to dust and take corrective measures, if needed.	No working during October-2024 to March-2025.																										
ix	A separate environmental management cell with suitable qualified personnel should be set-up under the control of a Senior Executive who will report directly to the Head of the Organization.	<p>A full-fledged Environment Management Cell (EMC) has been established to look after environment aspects headed by an experienced engineer with more than 20 years' experience in the field of environment in the rank of DGM who directly reports Head of Mines.</p> <p>In addition to the EMC at Mines level an Environment & lease department at Rourkela Steel Plant headed by a qualified person (M. Tech in Environmental Engineering) and experience environmental engineers who facilitate all the mines including MOM, Chiria mines in implementation and maintained of pollution control measures.</p>																										
x	The funds earmarked for environmental protection measures should be kept in separate account and should not be diverted for other purpose. Year wise expenditure should be reported to the Ministry of Environment and Forests and its Regional Office located at Bhubaneswar.	<p>There will be separate budget for Environment & Lease department. The allocated budget will be exclusively used for Environment & Lease expenses only. Year wise expenditure from 2013-14 on Environmental protection measures is as furnished below:-</p> <table><tr><th>Year</th><th>Approximate Expenditure</th></tr><tr><td>2024-25</td><td>74.69 Lakhs</td></tr><tr><td>2023-24</td><td>70.96 Lakhs</td></tr><tr><td>2022-23</td><td>58.97 Lakhs</td></tr><tr><td>2021-22</td><td>57.82 Lakhs</td></tr><tr><td>2020-21</td><td>53.67 Lakhs</td></tr><tr><td>2019-20</td><td>53.45Lakhs</td></tr><tr><td>2018-19</td><td>48.54 Lakhs</td></tr><tr><td>2017-18</td><td>50.84 Lakhs</td></tr><tr><td>2016-17</td><td>53.02 Lakhs</td></tr><tr><td>2015-16</td><td>44.60 Lakhs</td></tr><tr><td>2014-15</td><td>25.70 Lakhs</td></tr><tr><td>2013-14</td><td>42.00 Lakhs</td></tr></table>	Year	Approximate Expenditure	2024-25	74.69 Lakhs	2023-24	70.96 Lakhs	2022-23	58.97 Lakhs	2021-22	57.82 Lakhs	2020-21	53.67 Lakhs	2019-20	53.45Lakhs	2018-19	48.54 Lakhs	2017-18	50.84 Lakhs	2016-17	53.02 Lakhs	2015-16	44.60 Lakhs	2014-15	25.70 Lakhs	2013-14	42.00 Lakhs
Year	Approximate Expenditure																											
2024-25	74.69 Lakhs																											
2023-24	70.96 Lakhs																											
2022-23	58.97 Lakhs																											
2021-22	57.82 Lakhs																											
2020-21	53.67 Lakhs																											
2019-20	53.45Lakhs																											
2018-19	48.54 Lakhs																											
2017-18	50.84 Lakhs																											
2016-17	53.02 Lakhs																											
2015-16	44.60 Lakhs																											
2014-15	25.70 Lakhs																											
2013-14	42.00 Lakhs																											



Sl. No.	Condition	Compliance as on March' 2025
xi	The project authorities should inform to The Regional Office located at Bhubaneswar regarding date of financial closures and final approval of the project by the concerned authorities and the date of start of land development work.	Will be followed.
xii	The Regional Office of this Ministry located at Bhubaneswar shall monitor compliance of the stipulated conditions. The project authorities should extend full cooperation to the officer(s) of the Regional Office by furnishing the requisite date/information/monitoring reports.	Full co-operation is extended to the officers of the Regional Office, MoEF & CC, Ranchi, by furnishing the requisite data / information / monitoring reports.
xiii	The project proponent shall submit six monthly reports on the status of compliance of the stipulated EC conditions including results of monitored date (both in hard copies as well as by e-mail) to the Ministry of Environment and Forests, its Regional Office Bhubaneswar, The respective Zonal Office of Central Pollution Control Board the State Pollution Control Board. The proponent shall upload the status of compliance of the EC conditions, including results of monitored date on their website and shall update the same periodically. It shall simultaneously be sent to the Regional Office of the Ministry of Environment & Forests, Bhubaneswar, the respective Zonal Office of Central Pollution Control Board and State Pollution Control Board.	Six monthly compliance reports on the status of implementation of environmental safeguards are being submitted to MoEF&CC, New Delhi, Regional Office – MoEF&CC, Ranchi, Central Pollution Control Board and State Pollution Control Board. Copy of the compliance report including environmental quality data is being uploaded to the SAIL web site i.e. www.sail.co.in .
xiv	A copy of the clearance letter shall be sent by the proponent to concerned panchayat, Zila Parishad/Municipal Corporation, Urban Local Body and the Local NGO, if any from whom suggestions/representations, if any were received while processing the proposal. The clearance letter shall also be put on the website of the Company by the proponent.	The copy of Clearance letter was notified in the public places. The clearance letter has been put on the Company website.
xv	The State Pollution Control Board should display a copy of the clearance letter at the Regional Office, District Industry Centre and the Collector's office/Tehsildar's office for 30 days.	--
xvi	The environmental statement for each financial year ending 31 st March in Form-V as is mandated to be submitted by the project proponent to the concerned SPCB as prescribed under the	Environmental Statement for the financial year 2024-25 ending 31 st March, 2025 has been submitted to the Jharkhand State Pollution Control Board vide reference No:



Sl. No.	Condition	Compliance as on March' 2025
	Environment (Protection) Rules, 1986, as amended subsequently, shall also be put on the website of the company along with the status of compliance of EC conditions and shall also be sent to the Regional office of the MOEF, Bhubaneswar by e-mail.	MOM/PC/6/286, dated: 03-05-2025.
xvii	The project authorities should advertise at least in two local newspapers of the District or State in the project is located and widely circulated, one of which shall be in the vernacular language of the locality concerned, within 7 days of the issue of the clearance letter informing that the project has been accorded environmental clearance and a copy of the clearance letter is available with the State Pollution Control Board and also at web site of the Ministry of Environment and Forests at http://envfor.nic.in and a copy of the same should be forwarded to the Regional Office of this Ministry located at Bhubaneswar.	Advertisement was given in two local newspapers Hindustan times (English) and Dainik Jagaran (Local Language Hindi) within 7 days of the issue of the clearance letter.

Ravi Ranjan
30/5/25

(Ravi Ranjan)
General Manager (Mining)
Manoharpur Ore Mines, Chiria



Annexure – 1

GROUND WATER LEVEL MEASUREMENTS**A. Ground Water levels in and around the Mines**

Location ID	Location of Open Wells	Water level below the Ground Surface (in meters)	
		During Post Monsoon	During Winter
G1	Adjacent to community centre at Anqua	6.15	6.30
G2	Opposite to community centre at Anqua	6.30	6.40
G3	Near Anqua Model Steel Village Gate	1.90	2.10
G4	Siva Mandir	3.25	3.35
G5	Near CNI Church	7.95	8.00
G6	Near Bisra Chowk	1.70	1.80


Sl. No.	Location of Piezometer	Water level below the Ground Surface (in meters)	
		During Post Monsoon	During Post Monsoon
1	Chiria Village	4.10	4.10
2	Dhobil Village	3.70	3.70



Annexure-1



1. Piezometer at Chiria Village

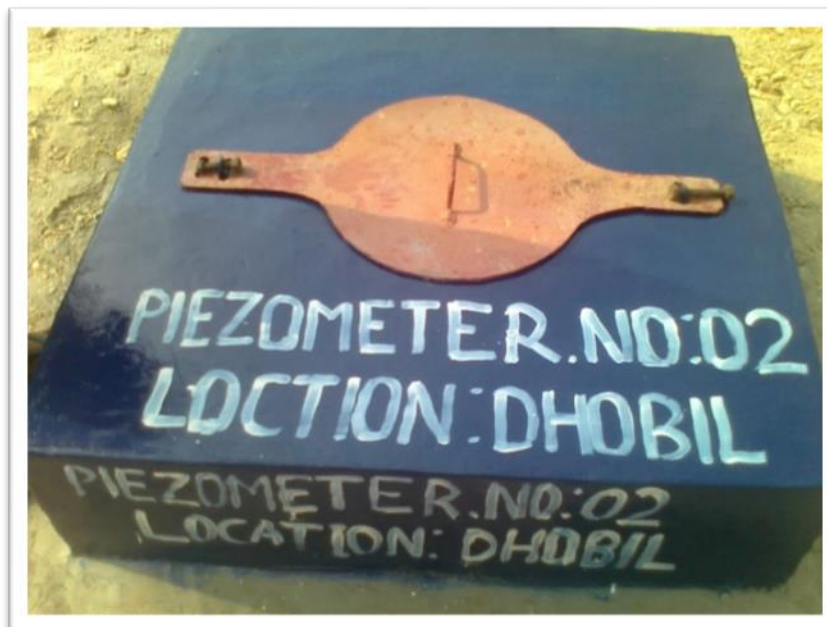

2. Piezometer at Dhobil Village



Installation of 5KLD STP & 5KLD ETP at SAIL Chiria Hospital



5KLD STP & 5KLD ETP at SAIL Chiria Hospital
